




SKY HARBOR RUNWAY RELOCATION NEWSLETTER

AVIATION SAFETY AND ENVIRONMENTAL PRESERVATION

May 11-17, 2020 – VOLUME 14

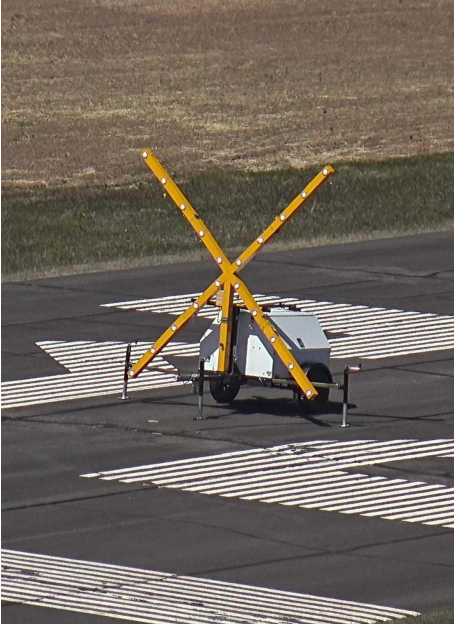

Existing Runway 14
May 12, 2020


Learn More:

Project newsletters including construction updates and photos will be distributed and posted on the airport website monthly. If you would like to be emailed the monthly newsletter, please contact Brandon Twedt (contact info below).

 skyharbor.duluthairport.com

Brandon Twedt, PE


Project Engineer
Short Elliott Hendrickson, Inc. (SEH)

 651-329-0133

 btwedt@sehinc.com

Brian Madsen

Sky Harbor Airport Manager
Duluth Airport Authority

 218-733-0078

 bmadsen@duluthairport.com

PROJECT UPDATE:

Week 1 (May 11-17) :

Removal of existing Runway 14-32. All pavements have been excavated and barged off site. Additionally, all existing airfield electrical was removed.

General site grading for new parallel taxiway.

Week 2 Schedule (May 18-23) :

Installing gravel base material for new runway and taxiways.

Paving test strip on parallel taxiway

General site grading



DRONE VIDEO AND 360 PHOTO LINKS

(click on links below)

<https://vimeo.com/417874224/d467e02517>

<https://sitescan.3dr.com/share/0f5e9f6f-cf1f-4546-b1e9-e5677981bce7>


<https://sitescan.3dr.com/share/e3732780-0fec-4e0f-b61e-9d7b6f1528ab>





SKY HARBOR RUNWAY RELOCATION NEWSLETTER

AVIATION SAFETY AND ENVIRONMENTAL PRESERVATION

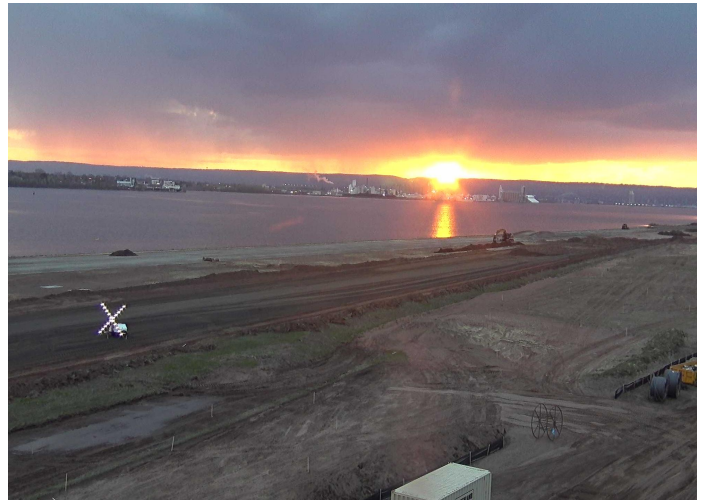

[SEHINC.COM/DRONES](https://www.sehinc.com/drones)

